




Monthly Executive Summary Report
Reflects Previous Month's Activity
Ashley River Creative Arts Elementary School
Constituent District 10

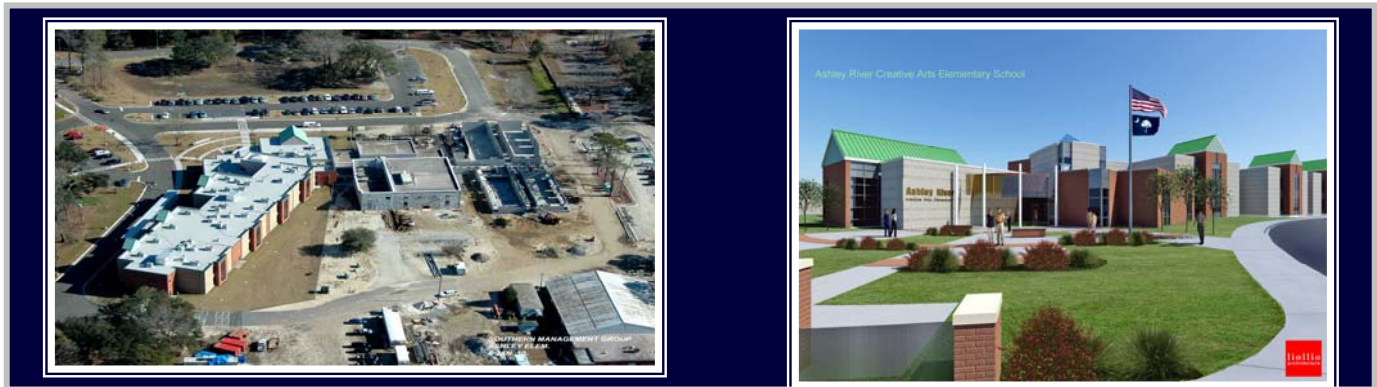

Project Team

Associate Superintendent: Dr. Doug Gepford
Principal: Jayne Ellicott
Project Manager: Jay Poston
Architectural Firm: Liollo Architecture
General Contractor: Martin Engineering, Inc.

Site Manager: Carl Dietz
Design Architect: Cherie Liollo

Project Scope:

Construction of a new two-story 600-student K-5 facility on the existing site while keeping the existing facility operational during the building process. The facility will include 29 instructional spaces with complementary support areas as indicated in the Educational Specifications. The existing facility will be demolished as required in accordance with the construction phases and completed at the end of the project.

Budget:

Original Budget: \$17.7 million
Revised Budget: \$19.9 million

Date: 5-10-2006
Date: 4-9-2007

Schedule:

Design: February 2008

Solicitation: April 2008

Construction: June 2010

Schedule Issues: Completion of south wing walls to bearing height (Weather delay)

Major Issues: Traffic coordination
Re-occupation of gymnasium

Achievements: South wing foundation slab & block masonry walls
South parking lot / storm drainage system
Portable relocation
North wing (Phase 2A) move-in
South wing demolition



Monthly Executive Summary Report
Reflects Previous Month's Activity
Ashley River Creative Arts Elementary School
Constituent District 10

Phasing/Mobile Classrooms:

Construction will be accomplished in phases utilizing additional mobile units on site to accommodate classroom spaces during the building process.

