




Monthly Executive Summary Report  
Reflects Previous Month's Activity

**Ashley River Creative Arts Elementary School**  
Constituent District 10

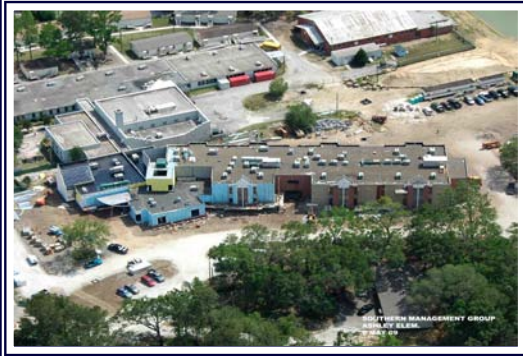

**Project Team**

**Associate Superintendent:** Dr. Doug Gepford

**Principal:** Jayne Ellicott

**Project Manager:** Jay Poston

**Architectural Firm:** Liollo Architecture

**General Contractor:** Martin Engineering, Inc.

**Site Manager:** Carl Dietz

**Design Architect:** Cherie Liollo

**Project Scope:**

Construction of a new two-story 600-student K-5 facility on the existing site while keeping the existing facility operational during the building process. The facility will include 29 instructional spaces with complementary support areas as indicated in the Educational Specifications. The existing facility will be demolished as required in accordance with the construction phases and completed at the end of the project.

**Budget:**

**Original Budget:** \$17.7 million

**Date:** 5-10-2006

**Revised Budget:** \$19.9 million

**Date:** 4-9-2007

**Schedule:**

**Design:** February 2008

**Solicitation:** April 2008

**Construction:** June 2010

**Schedule Issues:** Windows / Dry-in  
Painting

**Major Issues:** Summer move-in schedule  
Main Technology room renovation

**Achievements:** Built-up Roofing  
Permanent power connection / switch over  
Brick Veneer (80%)  
Metal studs  
Interior door frames



Monthly Executive Summary Report  
Reflects Previous Month's Activity

**Ashley River Creative Arts Elementary School**  
**Constituent District 10**

*Phasing/Mobile Classrooms:*

Construction will be accomplished in phases utilizing additional mobile units on site to accommodate classroom spaces during the building process.





Monthly Executive Summary Report  
Reflects Previous Month's Activity  
**Ashley River Creative Arts Elementary School**  
Constituent District 10

