



Monthly Executive Summary Report
Reflects Previous Month's Activity
Cario Middle School
Charleston County School District



Project Team

Associate Superintendent: Dr. Lynda Davis

Principal: Shari Bouts

Project Manager: Jack Burgess

Architectural Firm: HGBD Arch./Eng.

Contractor: Metro Contracting, Inc.

Site Manager: Stephanie Powell

Design Architect: Michael Pierce, AIA General

Project Scope: Construction of 12 additional classrooms at the rear of three wings on the existing facility. Each wing will receive a reading, math, general classroom and science lab. Additional features will include a teacher work space off the science lab, additional storage closet, corridor windows and new exists leading to connecting sidewalks.

Budget:

Original Budget: \$6 Million

Revised Budget: \$5 Million

Date: 5-10-2006

Date: 4-9-2007



Schedule:

Design: March 2007 Solicitation: June 2007 Construction: Complete August 2008

Schedule Issues: None at this time.




Major Issues: None at this time.

Achievements: The project is substantially complete and the punch list is underway.


Phasing/Mobile Classrooms: None required - Addition will not effect existing school operations.




Monthly Executive Summary Report
Reflects Previous Month's Activity
Cario Middle School
Charleston County School District

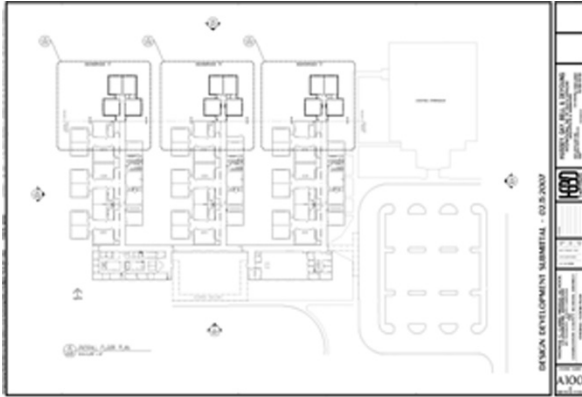


Overall Floor Plan

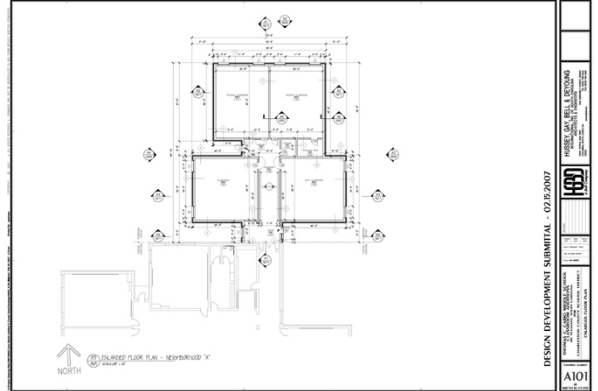

Addition(s) Typical Floor Plan

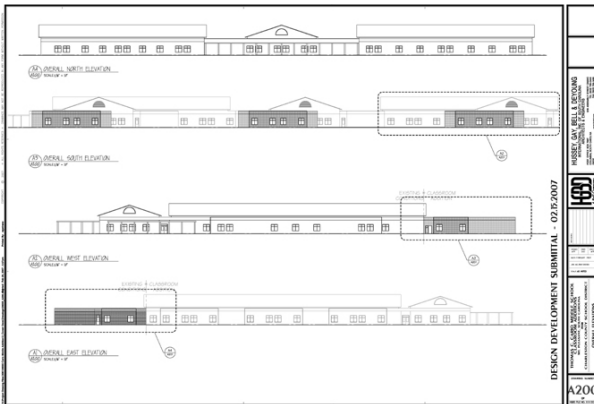

Elevation

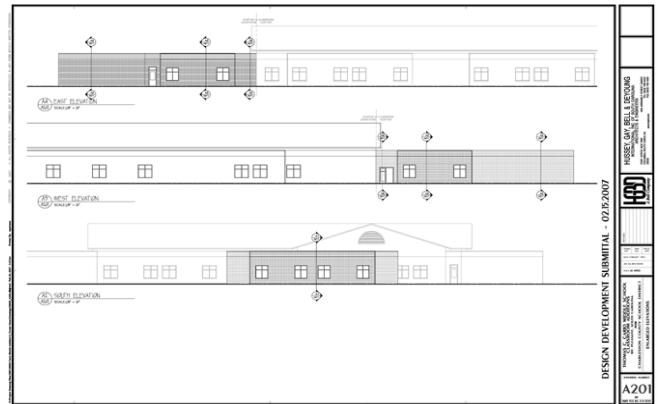

Elevation
