



Monthly Executive Summary Report  
Reflects Previous Month's Activity  
**Cario Middle School**  
Charleston County School District



***Project Team***

**Associate Superintendent: Dr. Lynda Davis**

**Principal: Carol Bartlett**

**Project Manager: Jack Burgess**

**Architectural Firm: HGBD Arch./Eng.**

**Contractor: *To Be Determined***

**Site Manager: Larry Jordan**

**Design Architect: Michael Pierce, AIA    General**

***Project Scope: Construction of 12 additional classrooms at the rear of three wings on the existing facility. Each wing will receive a reading, math, general classroom and science lab. Additional features will include a teacher work space off the science lab, additional storage closet, corridor windows and new exists leading to connecting sidewalks.***

***Budget:***

**Original Budget: \$6 Million**

**Revised Budget: \$5 Million**

**Date: 5-10-2006**

**Date: 4-9-2007**



***Schedule:***

**Design: March 2007    Solicitation: June 2007    Construction: Complete August 2008**

**Schedule Issues: None at this time.**




***Major Issues: Decisions Regarding Foundation Type completed. Project will be placed on wood pile foundation.***

***Achievements: Design Document Reviews and estimate completed. Project estimate is within budget.***


***Phasing/Mobile Classrooms: None required - Addition will not effect existing school operations.***




Monthly Executive Summary Report  
Reflects Previous Month's Activity  
**Cario Middle School**  
Charleston County School District

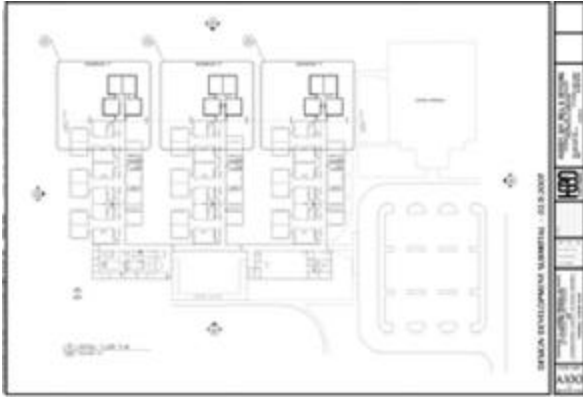


**Overall Floor Plan**

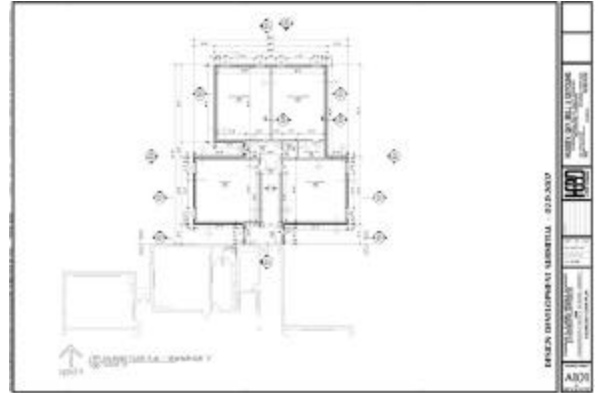

**Addition(s) Typical Floor Plan**

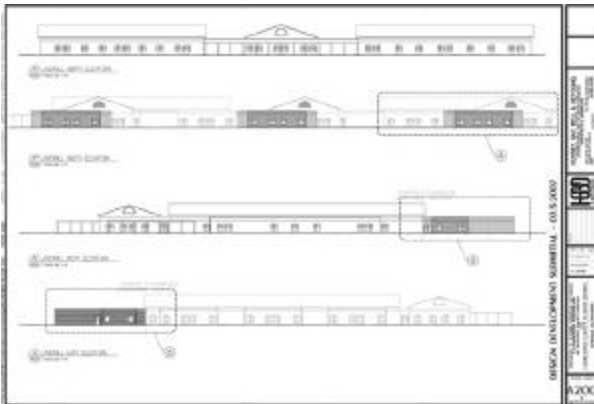

**Elevation**

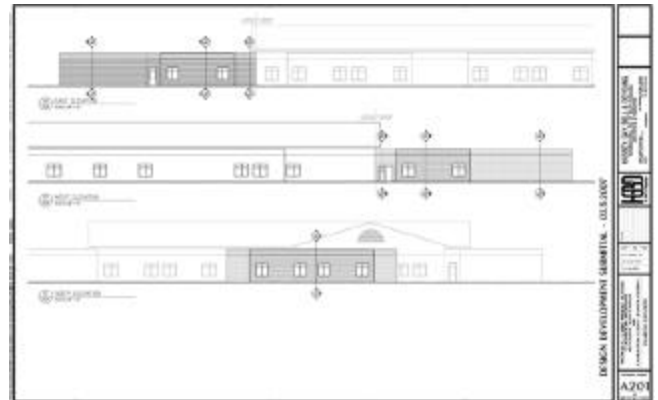

**Elevation**
