


### New Mamie Whitesides Elementary


#### Early Site Package

NM1000	Early Site Package Drawings Complete	0		02MAY08A
NM1001	Advertise for Bids	0		09MAY08A
NM1018	Pre Bid for Early Site Package	0	19MAY08A	
NM1019	Last Day for Questions	0		22MAY08A
NM1003	Bid & Award of Early Site Package	1	29MAY08A	03JUN08
NM1002	Receive Bids for Early Site Package	0	29MAY08A	
NM1004	Issue NTP for Early Site Package	0		24JUN08
NM1005	Construction Duration for Early Sitework	68	24JUN08	30AUG08
NM1006	Completion of Early SiteWork	0		30AUG08

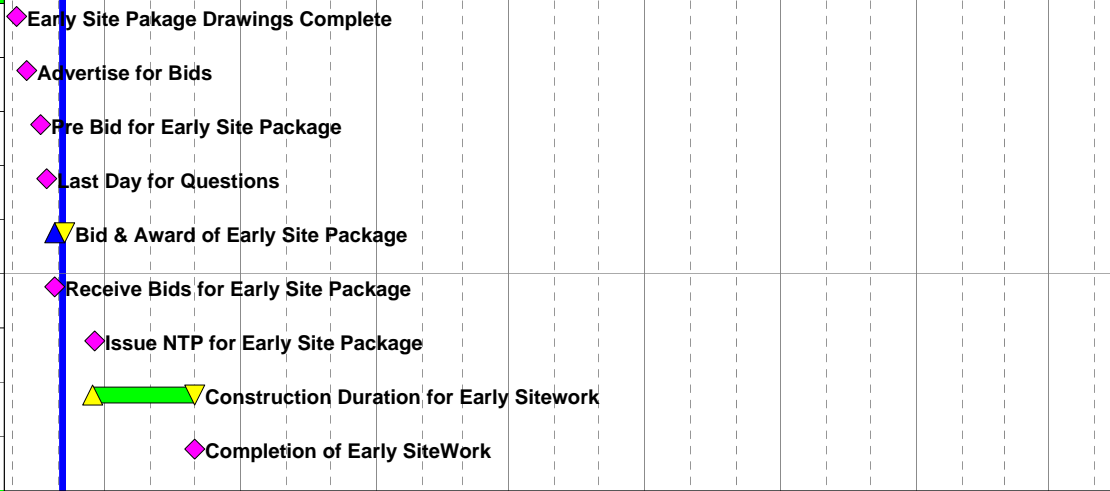


#### Building New Construction

NM1007	CD's Ready for Owner / OSF Review	0		02JUN08
NM1008	Progress Set of Plans	0		02JUN08
NM1009	Completion of CD's / Set to Print	0		14JUL08
NM1010	Receive Bids for New Construction	0		12AUG08
NM1011	Bid & Award for New Construction	16	12AUG08	27AUG08
NM1012	Issue NTP for New Construction	0		28AUG08
NM1013	Construction Duration of New Construction	464	28AUG08	04DEC09
NM1014	Substantial Completion of New Construction	0		04DEC09
NM1016	Owner Move-in to New School	30	05DEC09	03JAN10
NM1015	Final Completion of New Construction	0		03JAN10
NM1017	Owner Occupy Building	0		03JAN10

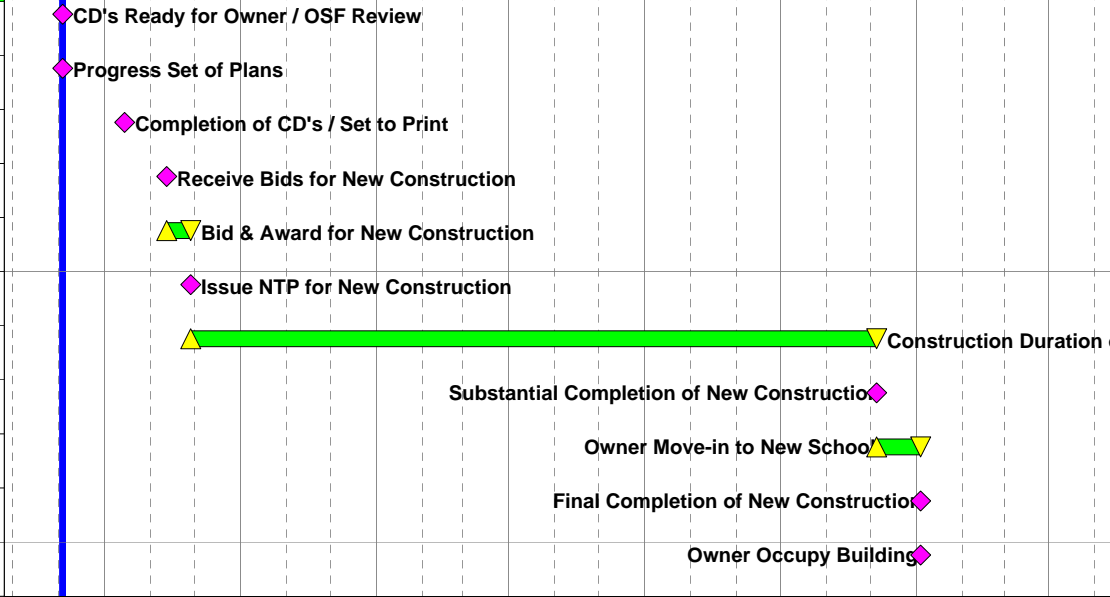

Start Date 25APR08  
 Finish Date 03JAN10  
 Data Date 03JUN08  
 Run Date 03JUN08 13:54



NMW1  
 Southern Management Group  
 New Mamie Whitesides Elementary  
 Classic Schedule Layout

Sheet 1 of 1	Date	Revision	Checked	Approved
	03JUN08			
